## WASH Sector Cox's Bazar

# WASH Site Profile - Zone EE

31315

7398

7892

4

Site Overview

# of individuals:

# of households:

# of individuals

# of shelters:

per shelter:

Ukhiya, Cox's Bazar, Bangladesh (December 2017) GPS Coordinates: 21.208792 92.147926

**Key WASH Infrastructure** 

1490

84%

962

525 (76%)

(70%)

# of latrines

(% functional):

% of safe latrines2:

# of handpumps

# of washrooms:

(% functional):




**Location Map** 

KHALI

#### **Summary**

This profile provides an overview of water, sanitation and hygiene (WASH) infrastructure within Zone EE in Ukhiya, Cox's Bazar. Primary data for this round was collected between 29 November and 17 December 2017.1 Findings should be considered indicative only.

## Access to Water

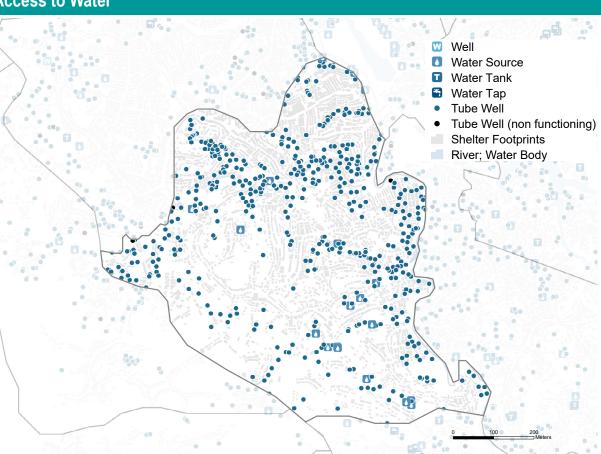

#### Three most commonly identified types of water points, by functionality

97% Handpump/tubewell	76%	24%	
2% Unimproved water source	100%	0%	Functional Non-functional
0.5% Well	67%	33%	-

#### Key sectoral achievements

	Target	Previous Round	Current Round	Achievement
# of people per functional hand pump	max. 500 <sup>3</sup>	295	79	
% of shelters within 200 metres of a functional hand pump⁴	100%	100%	100%	

Targets based on WASH Sector Standards/Indicators for the Rohingya response, Sphere Minimum Standards/Indicators as well as Department of Public Health and Environment (DPHE) Minimum Standards/Indicators • Minimum standard/indicator reached, • 75%-99% minimum standard/indicator reached, • 50-74% minimum standard/indicator reached, • Less than 50% of minimum standard/indicator reached


<sup>1</sup> REACH enumerators conducted a full sweep of all sites and camps (as per boundaries defined by ISCG) and used an Open Data Kit (ODK) form to log all key infrastructure observed during this sweep, with further details to be logged for WASH infrastructure. <sup>4</sup> Safe refers to fully covered latrines (i.e. a latrine with four walls, a roof and a door) <sup>3</sup> This farget is based on standards for the medium and long term (3 months +), for the immediate phase (0-3 months) it is 1000. <sup>4</sup> The distance is based on standards for the long term (6 months+), for the immediate phase (0-3 months) it is 750 metres and for the medium phase (3-6 months) 500 metres.







## Sanitation

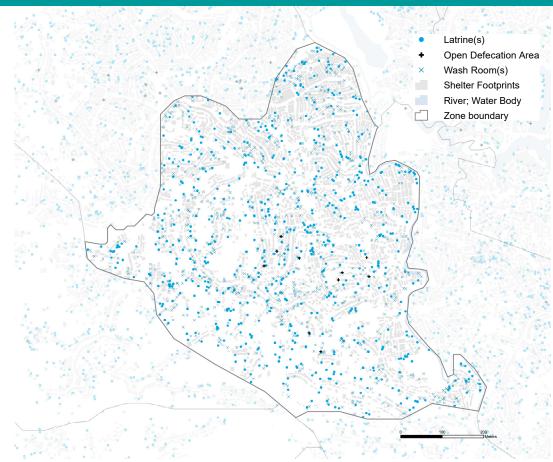

## Latrine characteristics

% of functional/non-functional latrines

70% functional (non-full) latrines30% non-functional latrines

% of safe/unsafe latrines:

84%Safe (roof, door, wall)16%Unsafe

% of latrines with/without lights

 0%
 With lights

 100%
 Without lights

### Key sectoral achievements

	Target	Previous Round	Current Round	Achievement
# of people per functional (non-full) latrine	max. 50 <sup>4</sup>	14	30	
# of people per safe latrine	N/A	10	25	N/A
% of shelters within 50 meters to a functional (non- full) latrine	100%	100%	100%	
% of latrines that are at least 10 meters away from a water point	100%	67%	69%	

Targets based on WASH Sector Standards/Indicators for Rohingya response, Sphere Minimum Standards/Indicators as well as DPHE Minimum Standards/ Indicators • Minimum standard/indicator reached, • 75%-99% minimum standard/indicator reached, • 50-74% minimum standard/indicator reached, • Less than 50% of minimum standard/indicator reached

<sup>4</sup> This target is based on standards for the long term (6 months +), for the immediate phase (0-3 months) it is 100 and for the medium phase (3-6 months) 75.



For more information, please contact REACH: bangladesh@reach-initiative.org

