WASH Sector Cox's Bazar

WASH Site Profile - Camp 02W
Ukhia, Cox's Bazar, Bangladesh (July 2018)
GPS Coordinates: 21.2089, 92.1583

Summary

This profile provides an overview of water, sanitation and hygiene (WASH) infrastructure within Camp 02W in Ukhia, Cox's Bazar. Primary data for this round was collected from 29th May to 22nd July 2018.[1] Findings should be considered indicative only. Full camp dataset is available on HDX.

## Site Overview

# of individuals:	25,069
# of households:	5,725
# of shelters:	4,683
# of individuals per shelter:	5.4

Key WASH Infrastructure

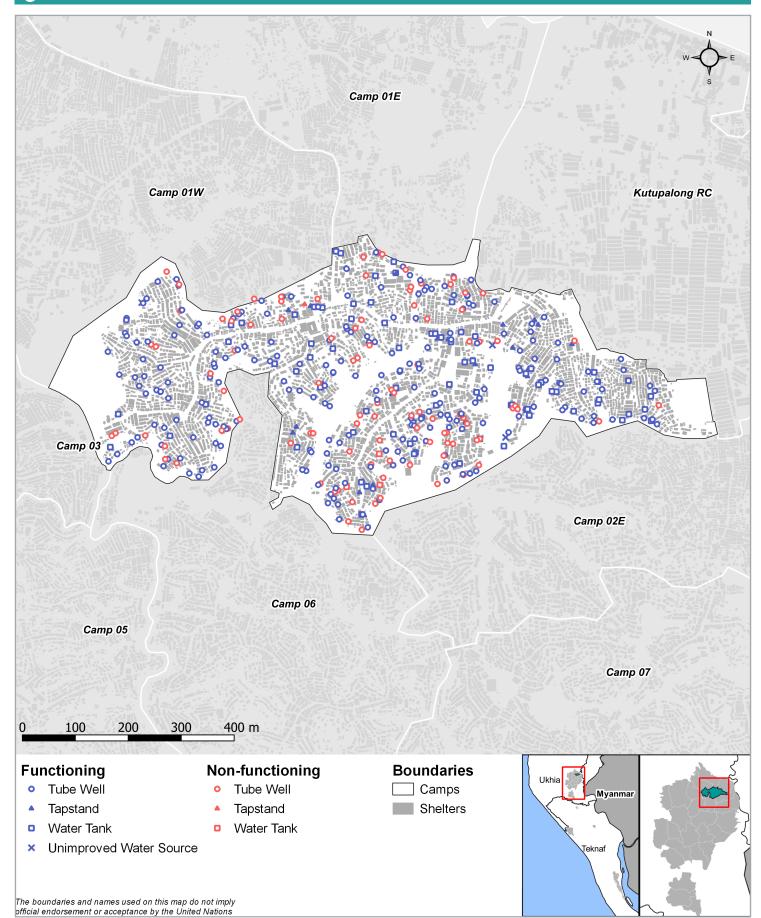|	
# of latrines: (% functional and safe[2]):	1,039 (61%)
# of improved water sources:[3] (% functional):	428 (76%)
# of washrooms:	496

Location Map
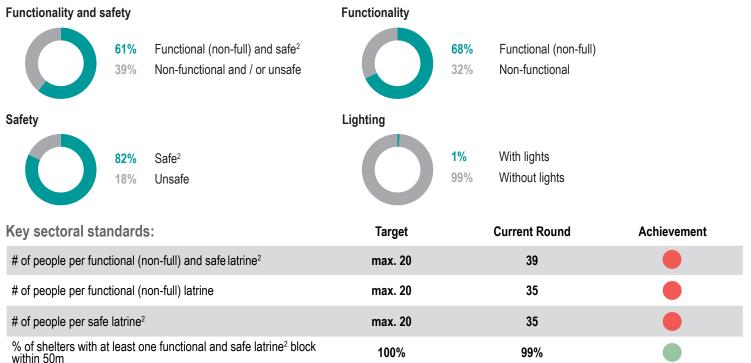
Water Access

Three most commonly identified types of water points, by functionality:

		Functional	Non-functional
75%	Handpump / tube well	69%	31%
19%	Water tank	96%	4%
5%	Tapstand	95%	5%

Legend: ■ Functional ■ Non-functional

Key sectoral standards:

	Target	Current Round	Achievement
# of people per functional improved water source	max. 250	77	🟢
% of shelters with at least 1 functional improved water source[3] within 200m	100%	100%	🟢
% of functional improved water sources with no latrine within 10m	100%	51%	🟠

Sanitation

Latrine characteristics:

Functionality and safety

61%	Functional (non-full) and safe[2]
39%	Non-functional and / or unsafe

Functionality

68%	Functional (non-full)
32%	Non-functional

Safety

82%	Safe[2]
18%	Unsafe

Lighting

1%	With lights
99%	Without lights

Key sectoral standards:

	Target	Current Round	Achievement
# of people per functional (non-full) and safe latrine[2]	max. 20	39	🔴
# of people per functional (non-full) latrine	max. 20	35	🔴
# of people per safe latrine[2]	max. 20	35	🔴
% of shelters with at least one functional and safe latrine[2] block within 50m	100%	99%	🟢

Targets based on long term WASH Sector Standards / Indicators for the Rohingya response, Sphere Minimum Standards as well as Department of Public Health and Environment (DPHE) Minimum Standards. ●Minimum standard/indicator reached, ●75%-99% minimum standard/indicator reached, ●50-74% minimum standard/indicator reached, ●Less than 50% of minimum standard/indicator reached.

1. REACH enumerators conducted a full sweep of all sites and camps (as per boundaries defined by ISCG) and used an Open Data Kit (ODK) form to log all key infrastructure observed during this sweep, with further details to be logged for WASH infrastructure.
2. Safe refers to fully covered latrines (i.e. a latrine with four walls, a roof and a lockable door).
3. This includes handpumps / tube wells, tapstands and water tanks.

WASH Sector
Cox's Bazar

Water Access

Camp 01E

Camp 01W

Kutupalong RC

Camp 03

Camp 02E

Camp 06

Camp 05

Camp 07

0   100   200   300   400 m

Functioning
- ○ Tube Well
- ▲ Tapstand
- ◻ Water Tank
- ✕ Unimproved Water Source

Non-functioning
- ○ Tube Well
- ▲ Tapstand
- ◻ Water Tank

Boundaries
- ☐ Camps
- ▮ Shelters

Ukhia

Myanmar

Teknaf

The boundaries and names used on this map do not imply official endorsement or acceptance by the United Nations

WASH Sector
Cox's Bazar

Sanitation

Camp 01E

Camp 01W

Kutupalong RC

Camp 03

Camp 02E

Camp 06

Camp 05

Camp 07

0   100   200   300   400 m

Functioning
- ☐ Latrines
- ▲ WASH Room

Non-functioning
- ☐ Latrines
- ▲ WASH Room

Boundaries
- ☐ Camps
- ■ Shelters

Ukhia
Myanmar
Teknaf
